

Drilling Mud Report(Off Shore)

Engineer H.Ito
M.Sawaguchi

No. _____ Date 7, December, 2013 TOTAL Depth(MSL) _____ m
Company MQJ Well Name C0002N (NT3-01) BRT Depth: _____ m, SSL Depth: _____ m

Casing Program		Mud Volume & Bit Data		Pump Data		String Data		Circulation Data (min)	
Conductor	36 in 2,121.5 m	Riser Vol. (m³) :	392	Pump No.1 (l/st) :	19.45	DP Size (in) :	5	Surface to Bit :	
Intermediate	20 in 2,827.8 m	CSG Vol. (m³) :		Pump No.2 (l/st) :	19.45	DC1 Size (in) :	8.5	Bottom's Up :	
Intermediate	13.375 in 3,976.5 m	B/Hole Vol. (m³) :		Pump No.3 (l/st) :	19.45	DC2 Size (in) :		Surf to Surf :	
Intermediate	in m	Disp Vol. (m³) :		P/Speed No.1 (spm) :		A/Vel DP (ft/min) :		System Total :	
Intermediate	in m	T/Circ Vol. (m³) :	492	P/Speed No.2 (spm) :		A/Vel DC1(ft/min) :			
Intermediate	in m	Pit Vol. (m³) :	100	P/Speed No.3 (spm) :		A/Vel Riser(ft/min) :			
Production	in m	Bit Size (inch) :	12.25	Rate (gal/min) :				P/ Press(Mpa) :	12.4

Mud Type:	KNPP	Mud Properties				Materials Name		Daily Amount	Total Amount	Daily Cost
Time (Sampling : Suction)		3:00		17:00		Tel-Bar				
Depth (m)		Pit		Pit		Kunigel VO (Bulk)				
Mud Weight (SG/PPG)		1.15 9.6	1.15 9.6			NaCl				
Funnel Viscosity(sec./qt.)		82		80		KCL				
A.V(cps) at / cent.		51.5		51 /25.5		Tel-Polymer DX				
P.V(cps)		35		36 / 19		Tel-Polymer L				
Y.V(lb/100ft²)		33		30 / 13		Tel-Polymer H				
10"Gel(lb/100ft²)		3		3 / 2		XCD-Polymer				
10'Gel(lb/100ft²)		6		6 / 6		Soda Ash				
API Filtrate(cc/30min.)		3.7		3.7		Caustic potash				
Cake Thickness(mm)		0.5		0.5		Clean Lube				
pH(-)		12.2		12.2		Tel Clean				
Pf(cc)		0.3		0.3		Bi-Carbonate				
Pm(cc)		5.7		5.7		Lime				
Mf(cc)		0.6		0.6		Defoamer 30C				
Cl (mg/l)		78,100		78,100		Telnite GXL				
Sand Content(%)		0.3		0.3		Tel-DD				
Oil Content(% Vol.)		0		0		Caustic soda				
Solid Content(% Vol.)		8		8		Lignite NC				
M.B.C.(cc/cc.mud)		1.00		1.00		Astex S				
Temperature(in/out cent.)		16		15						
HT-HP Filtrate(cc)						Tel Stop G				
HT-HP Filtrate Cake(mm)						Tel Stop P				
K' (mg/l)		32,400		31,800		Tel Mica C				
Ca ⁺⁺ /Mg ⁺⁺ (mg/l)		120		120		Tel Mica M				
n Value(600rpm/300rpm)		0.60		0.67		Tel Mica F				
k Value(600rpm/300rpm)		1.62		0.48		Tel Plug C				
LGS/Drill Solids(% Vol.)		1.3 0.8	1.4 0.8			Tel Plug M				
						Tel Plug F				
						Tan Cal M				
						Tan Cal F				
						Tan Cal FF				
						EZ Spot (gal/drm)				
						Speeder P				
						Speeder X				

Well Summary

Wire line job.Run CBL-VDL-CCI-GR to3925m.Run junk basket and gauge ring to3925m.
Run bridge plug.Set bridge plug at 3,918.6m. Pressure test bridge plug.
Make up 11-3/4"Flat bottom mill and RH.


Today's lost mud --m3. (Total 481m3).

On hand and Remarks

1.11sg KNPP mud : 470m3 @Re#1, Re#2 and Re#3
1.16sg Hi-vis mud : 27m3 @Act#1
1.13sg 20%LCM mud :24m3 @Act#3

Today's lost mud --m3. (Total 481m3).

Shale Shaker							De-Sander		Mud Cleaner		Centrifuge		
No.	#.1	#.2	#.3	#.4	#.5	#.6	#.1	#.2	#.1	#.2	#.1	#.2	#.3
Top	20	20	20	20	20	20							
Btm1	180	180	145	145	180	180					ON	OFF	OFF
Btm2													
Daily Cost													
Total Cost													



BALLAST REPORT(Off Shore)

NO. _____

Well Name C0002N (NT3-01)

DATE 7, Dec, 13

TIME 24:00

Active Tank

Tank Name	Status	M/W	Vol.	Monitor	Lo Limit	Remarks
Active #1	Hi-Vis mud	1.16sg	27.0KL			
Active #2	Empty					
Active #3	20%LCM mud	1.13sg	24.0KL			
Active #4	KNPP	1.15sg	42.0KL			Circ mud
Active #5	KNPP	1.15sg	42.0KL			Circ mud
Active #6	Return SW	1.03sg	30.0KL			
Chemical	Empty					
Slug	Slug mud	1.38sg	13.0KL			

Chemical Tank


Tank Name	Status	Weight	Monitor
Storage #1	Barite	134,000kg	
Storage #2	Barite	15,000kg	
Storage #3	Barite		
Storage #4	Barite		
Storage #5	Bentonite	0kg	
Storage #6	Bentonite		
Daily Tank #1	Bentonite	10,000kg	
Daily Tank #2	Barite	40,000kg	
Bar/Surge #1	Barite	2,500kg	
Bar/Surge #2	Barite	1,500kg	
Gel/Surge #2	Bentonite	800kg	

Chemical Tank Total WT 203.8 ton

Reserve Tank & Solid Control Tank

Tank Name	Status	M/W	Vol.	Monitor	Lo Limit	Remarks
Reserve #1	KNPP	1.11sg	170.0KL			
Reserve #2	KNPP	1.11sg	180.0KL			
Reserve #3	KNPP	1.11sg	120.0KL			
Reserve #4	Return SW	1.03sg	156.0KL			
Reserve #5	Empty					
Reserve #6	Empty					
Reserve #7	Return SW	1.03sg	152.0KL			
Reserve #8	Return SW	1.03sg	182.0KL			
Sand Trap	KNPP	1.15sg	10.0KL			
Degasser	KNPP	1.15sg	10.0KL			
Desander	KNPP	1.15sg	10.0KL			
Desilter	KNPP	1.15sg	10.0KL			
Soli/con CF	KNPP	1.15sg	10.0KL			
Mud Return	KNPP	1.15sg	10.0KL			
Barite Rec CF	Drill water	1.00sg				

Mud Tank Total WT 1299.3 ton

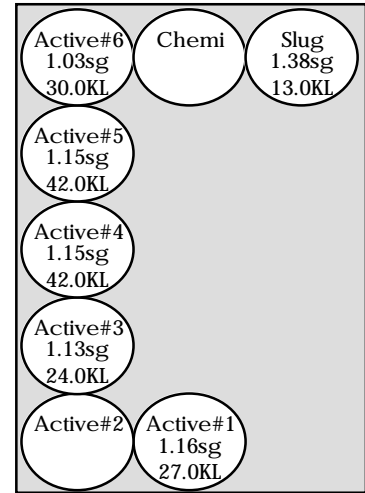

Bulk Material

Unit(kg)

Materials Name	Receive	Total Receive	Use	Total Use	On Hand	Remarks
Tel-Bar		263,240		70,240	193,000	
Kunigel VO (Bulk)		29,460		18,660	10,800	

Total SX ROOM Weight 136.8 ton

Total Weight 1,639.9 ton

Made by : M.sawaguchi
